


U.S. Office of Personnel Management Data Center Consolidation Roadmap

Please see below for a text version of the roadmap.

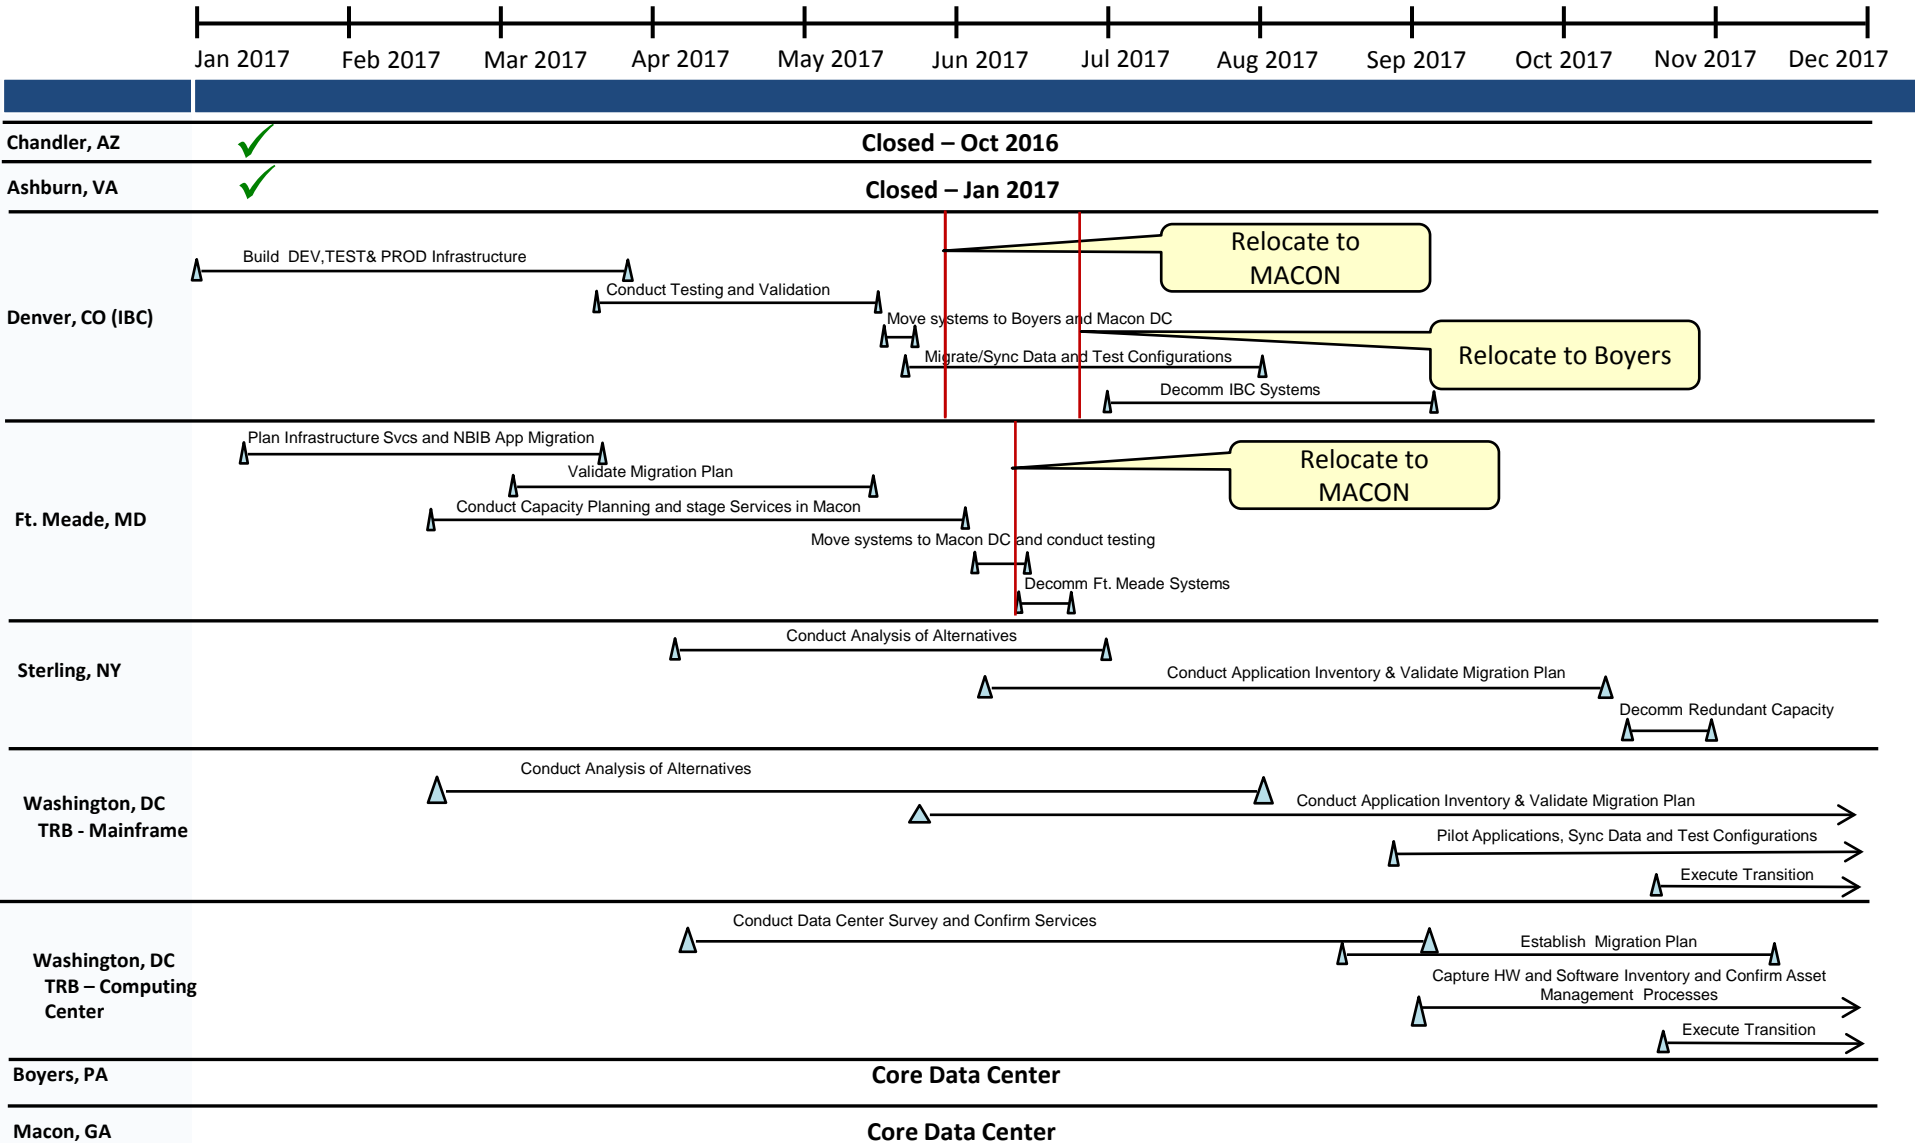

All dates are in 2017 unless otherwise noted.

Chandler, Arizona

Closed in October 2016.

Ashburn, Virginia

Closed in January.

Denver, Colorado (IBC)

1. Build development, test, and production infrastructure: January to April
2. Conduct testing and validation: March to May
3. Move systems to Boyers and Macon data centers: May
4. Migrate and sync data and test configurations: May to August
5. Relocate to Macon: June
6. Relocate to Boyers: July
7. Decommission IBC Systems: July to September

Fort Meade, Maryland

1. Plan infrastructure services and NBIB application migration: January to April
2. Conduct capacity planning and stage services in Macon: February to June
3. Validate migration plan: March to May
4. Move systems to Macon and DC and conduct testing: June
5. Relocate to Macon: June
6. Decommission Fort Meade systems: June

Sterling, New York

1. Conduct Analysis of Alternatives: April to July
2. Conduct application inventory and validate migration plan: June to October
3. Decommission redundant capacity: November

Washington, DC

Theodore Roosevelt Building Mainframe

1. Conduct Analysis of Alternatives: February to August
2. Conduct application inventory and validate migration plan: May to after December
3. Pilot applications, sync data, and test configurations: August to after December
4. Execute transition: October to after December

Theodore Roosevelt Building Computing Center

1. Conduct data center survey and confirm services: April to September
2. Establish migration plan: August to December
3. Capture hardware and software inventory and confirm asset management processes: September to after December
4. Execute transition: October to after December

Boyers, Pennsylvania

Core data center; will not close.

Macon, Georgia

Core data center; will not close.
