


# U.S. Office of Personnel Management Data Center Consolidation Roadmap

Please see below for a text version of the roadmap.

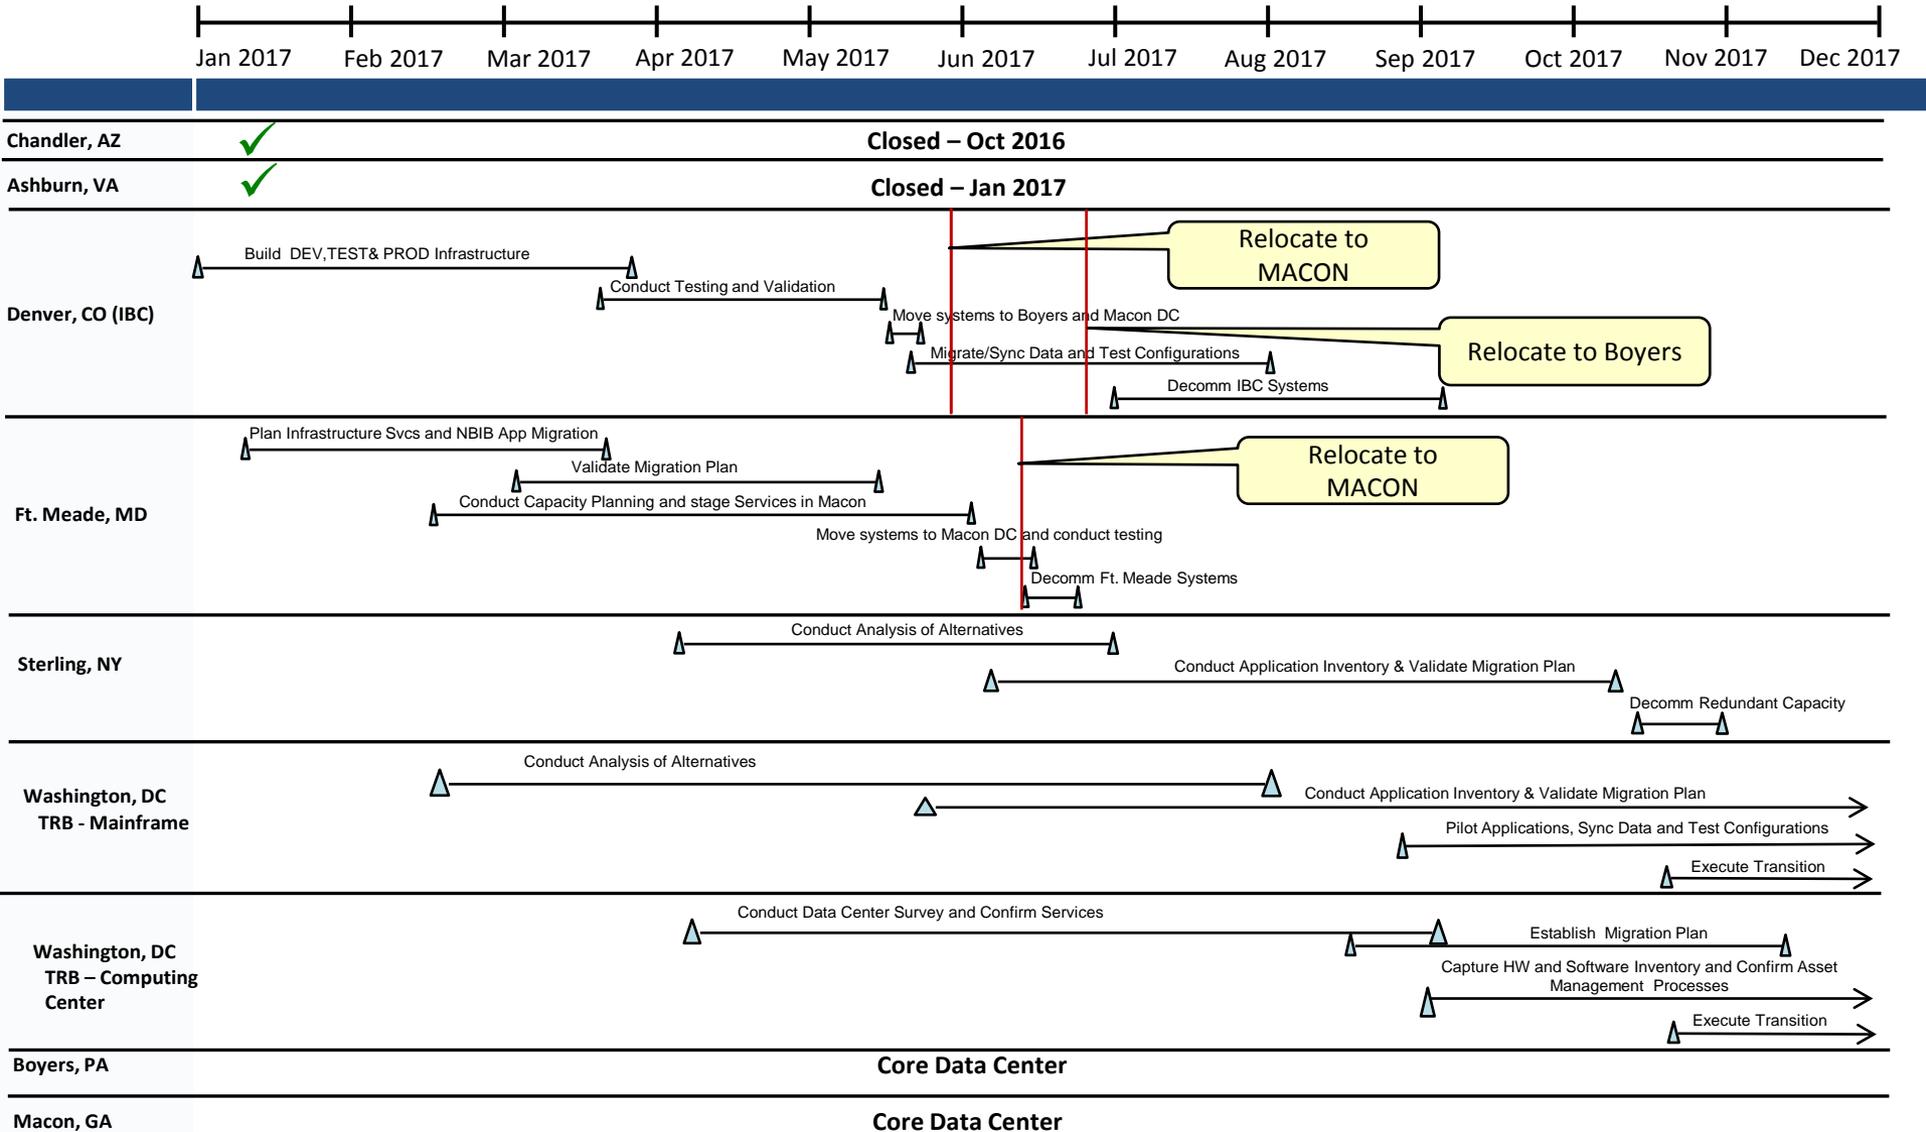

All dates are in 2017 unless otherwise noted.

### **Chandler, Arizona**

Closed in October 2016.

### **Ashburn, Virginia**

Closed in January.

### **Denver, Colorado (IBC)**

1. Build development, test, and production infrastructure: January to April
2. Conduct testing and validation: March to May
3. Move systems to Boyers and Macon data centers: May
4. Migrate and sync data and test configurations: May to August
5. Relocate to Macon: June
6. Relocate to Boyers: July
7. Decommission IBC Systems: July to September

### **Fort Meade, Maryland**

1. Plan infrastructure services and NBIB application migration: January to April
2. Conduct capacity planning and stage services in Macon: February to June
3. Validate migration plan: March to May
4. Move systems to Macon and DC and conduct testing: June
5. Relocate to Macon: June
6. Decommission Fort Meade systems: June

### **Sterling, New York**

1. Conduct Analysis of Alternatives: April to July
2. Conduct application inventory and validate migration plan: June to October
3. Decommission redundant capacity: November

## **Washington, DC**

### *Theodore Roosevelt Building Mainframe*

1. Conduct Analysis of Alternatives: February to August
2. Conduct application inventory and validate migration plan: May to after December
3. Pilot applications, sync data, and test configurations: August to after December
4. Execute transition: October to after December

### *Theodore Roosevelt Building Computing Center*

1. Conduct data center survey and confirm services: April to September
2. Establish migration plan: August to December
3. Capture hardware and software inventory and confirm asset management processes: September to after December
4. Execute transition: October to after December

## **Boyers, Pennsylvania**

Core data center; will not close.

## **Macon, Georgia**

Core data center; will not close.
